

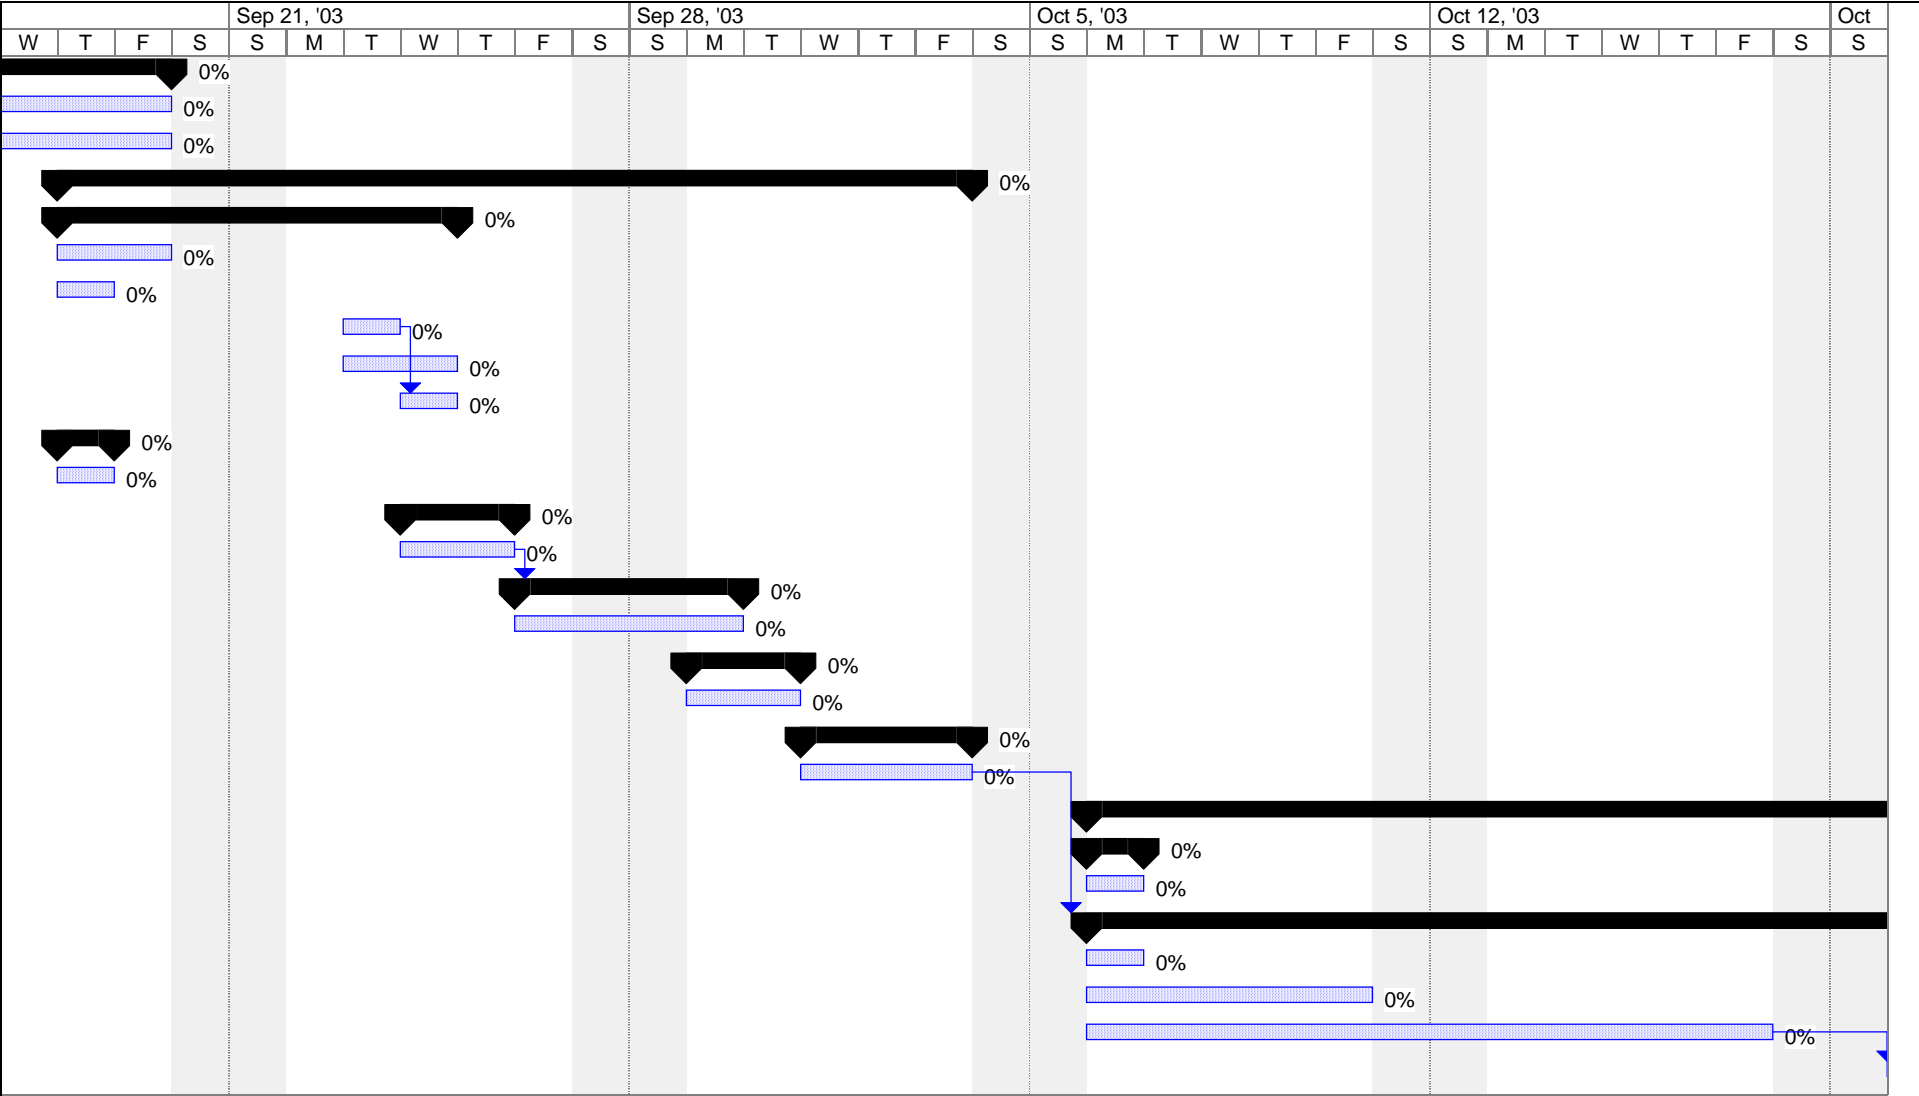


ID	Task Name	Duration	Start	Finish	4, '03	
					M	T
1	Planning	4 days	Tue 9/16/03	Fri 9/19/03		
2	Prepare Vision and Direction statement.	4 days	Tue 9/16/03	Fri 9/19/03		
3	Prepare project plan with milestones and deadlines.	3 days	Wed 9/17/03	Fri 9/19/03		
4	Requirements Gathering/ Definition	12 days?	Thu 9/18/03	Fri 10/3/03		
5	Focus Group	5 days	Thu 9/18/03	Wed 9/24/03		
6	Prepare Focus Group Questions	2 days	Thu 9/18/03	Fri 9/19/03		
7	Set up Focus Group Meeting	1 day	Thu 9/18/03	Thu 9/18/03		
8	Meet with Focus Group	1 day	Tue 9/23/03	Tue 9/23/03		
9	Analyze Results and prepare typewritten notes	2 days	Tue 9/23/03	Wed 9/24/03		
#	Send follow up thank you notes	1 day	Wed 9/24/03	Wed 9/24/03		
#	Review other Security Websites	1 day?	Thu 9/18/03	Thu 9/18/03		
#	Take notes of possible content and layout designs to use for FSA website.	1 day?	Thu 9/18/03	Thu 9/18/03		
#	Audit OCIO website	2 days	Wed 9/24/03	Thu 9/25/03		
#	Prepare list of FSA security references to be updated	2 days	Wed 9/24/03	Thu 9/25/03		
#	Audit FSA website	2 days	Fri 9/26/03	Mon 9/29/03		
#	Prepare list of FSA security references to be updated	2 days	Fri 9/26/03	Mon 9/29/03		
#	Intranet Meeting w/ FSA Intranet employees	2 days	Mon 9/29/03	Tue 9/30/03		
#	Prepare list of questions for meeting	2 days	Mon 9/29/03	Tue 9/30/03		
#	Audit and Analyze existing FSA SSO web portal	3 days	Wed 10/1/03	Fri 10/3/03		
#	Determine what current features of site to retain.	3 days	Wed 10/1/03	Fri 10/3/03		
#	Design	21 days?	Mon 10/6/03	Mon 11/3/03		
#	Meeting with Personnel Security Representative	1 day?	Mon 10/6/03	Mon 10/6/03		
#	Prepare questions for meeting with Monica.	1 day?	Mon 10/6/03	Mon 10/6/03		
#	Document Preparation for website	14 days?	Mon 10/6/03	Thu 10/23/03		
#	Determine sections for website	1 day?	Mon 10/6/03	Mon 10/6/03		
#	Determine which documents to use-which documents go in which section.	5 days	Mon 10/6/03	Fri 10/10/03		
#	Locate versions and gather in central location.	10 days	Mon 10/6/03	Fri 10/17/03		
#	Create summaries of each document that will be on the website	1 day?	Mon 10/20/03	Mon 10/20/03		

Project: Project plan for security toolkit Date: Mon 4/12/04	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			



Project: Project plan for security toolkit Date: Mon 4/12/04	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

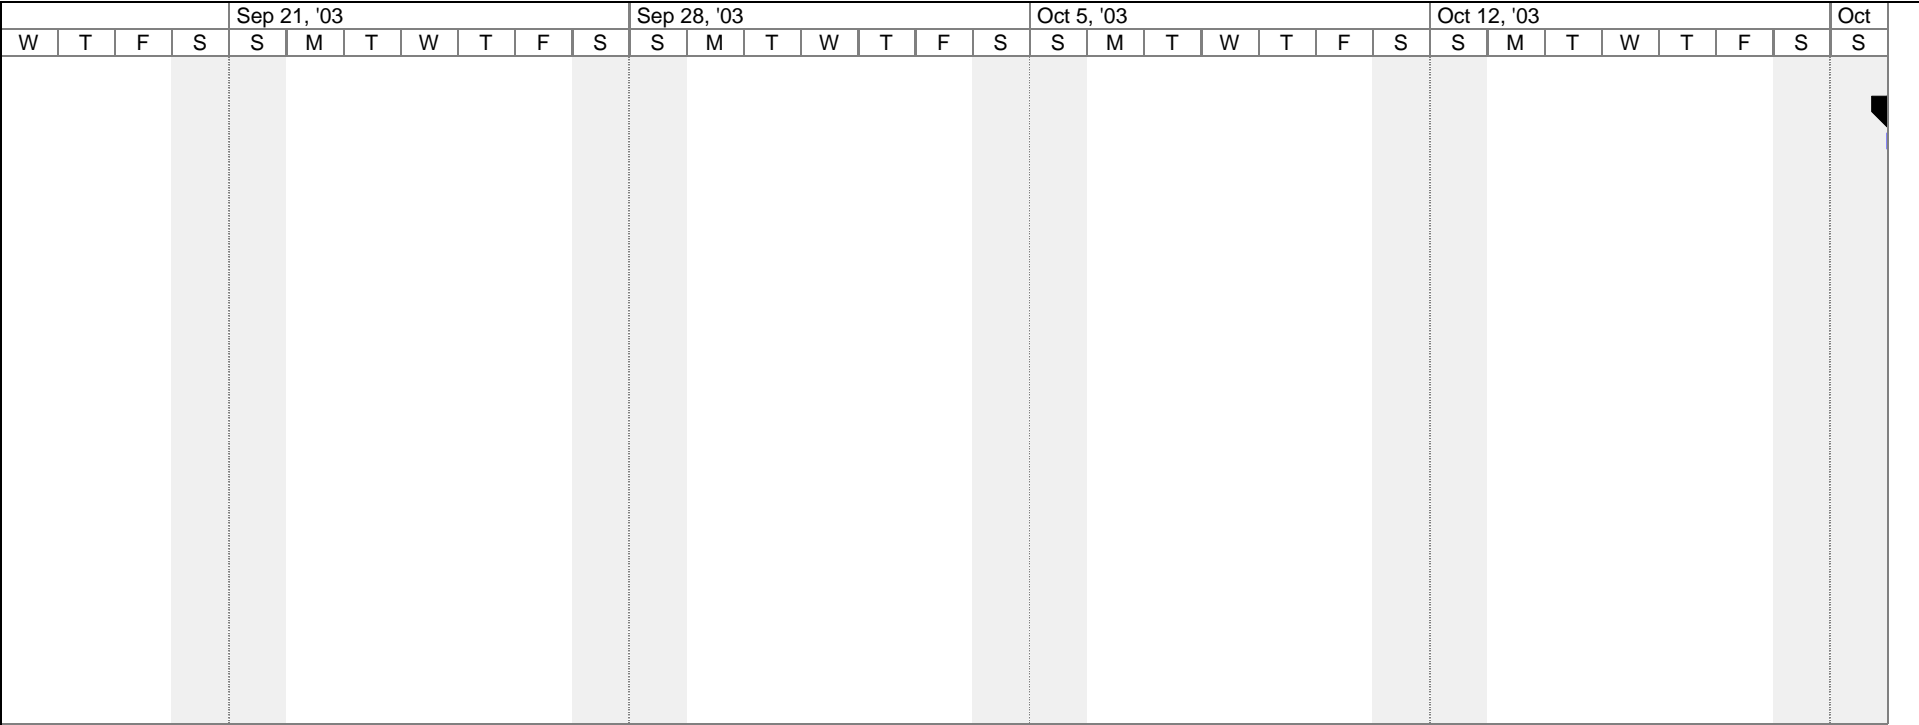

Project: Project plan for security toolkit
Date: Mon 4/12/04

Critical

Critical Split

Critical Progress

Task

Split

Task Progress

Baseline

Baseline Split

Baseline Milestone

Milestone

Summary Progress

Summary

Project Summary

External Tasks

External Milestone

Deadline

