



WAN IPT Statement of Objectives

The charter of the WAN IPT is to re-engineer the work that is currently performed by the Title IV WAN contract. The team will perform their work with the following objectives in mind:

- SFA Data transmissions are to be moved to the Internet
- ◆ The Title IV WAN contract is to be "tombstoned"
- ◆ Transition of each component of the Title IV WAN contract to other areas must occur smoothly and without interruption of current services
- ◆ The team's recommendations must support the future vision of SFA's technical architecture



WAN IPT Approach

- ✓ Core team to set priorities and take overall view across sub-teams
- ✓ Core team will coordinate with Kay Jacks (IPT Sponsor), Steve Hawald (CIO), and Candace Hardesty (Acquisitions and Contract Performance)
- ✓ Sub-teams to address each of the 9 major components of Title IV WAN
- ✓ First priority is "SFA to the Internet"
- ✓ Other objectives to be worked on concurrently with "SFA to the Internet"



Core Team

✓ Keith Wilson SFA CIO

✓ Yolanda Brooks SFA CIO

✓ TBD SFA CFO

✓ Jane Holman SFA School Channel (recommended)

✓ Jeanne Saunders SFA Student Channel

✓ TBD SFA Financial Partners Channel

✓ TBD SFA Acquisitions and Contract Performance

✓ Peter Elms Modernization Partner


✓ Jeff Sheetz Modernization Partner

✓ Sharon Barfield Modernization Partner

✓ Connie Donald WAN Program Manager



WAN IPT Focus Areas

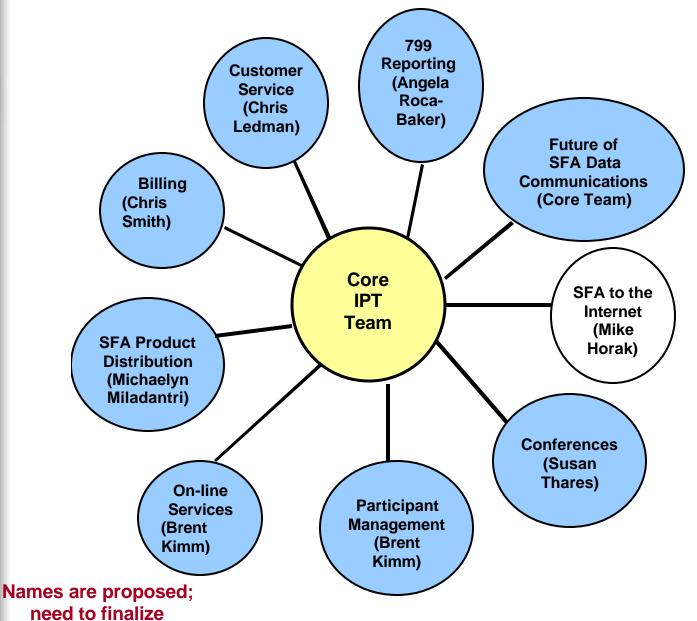



Title IV WAN IPT Road Map

Procurement 7	Valeiala fan	\mathbf{T}
Procurement	venicie ior	IP I
I I OCUI CITICIT	V CHICK IO	

Develop Statement of Objectives	10/13/2000
Develop Task Order Proposal	10/27/2000
Gain Mgmt Approval / Funding	11/8/2000

Core IPT Activities

Form Team	10/13/2000
Identify Team Leads	10/13/2000
Management Council Presentation	10/19/2000
Develop Cost Baseline	11/15/2000
* Develop Business Case	1/15/2001
Develop Sequencing Plan	1/31/2001

* Details Follow on next three slides



Business Case Details

11/29/2000
12/13/2000
12/20/2000
12/27/2000
1/16/2001
11/30/2000
12/28/2000
1/5/2001
1/19/2001
1/24/2001
12/13/2000
1/15/2001
1/22/2001
2/8/2001
2/12/2001



Business Case Details

Customer Service	
Business case	11/30/2000
Authorize business plan	12/7/2000
Contract negotiations	12/15/2000
Begin business plan execution	1/2/2001
SFA Product Distribution	
Business case	12/28/2000
Authorize business plan	1/5/2001
Contract negotiations	1/19/2001
Begin business plan execution	1/24/2001
Billing *	
Business case	1/15/2001
Authorize business case	1/22/2001
Contract negotiations	2/5/2001
Execute business plan	2/8/2001

Assumption - Dates dependent on outcome of SFA to the Internet, Participant Management, and Customer Service business plans



Business Case Details

799 Reporting	
Focus Group	<tbd></tbd>
Business case	<tbd></tbd>
Authorize business case	<tbd></tbd>
Contract negotiations	<tbd></tbd>
Begin business plan execution	<tbd></tbd>
Conferences	
Business case	11/30/2001
Authorize business case	12/7/2001
Contract negotiations	12/15/2001
Begin business plan execution	1/2/2001
Future of SFA Data Comm.	
Business case	<tbd></tbd>
Authorize business case	<tbd></tbd>
Contract negotiations	<tbd></tbd>
Begin business plan execution	<tbd></tbd>



Questions?
